HERCULES
A SENNECA COMPANY

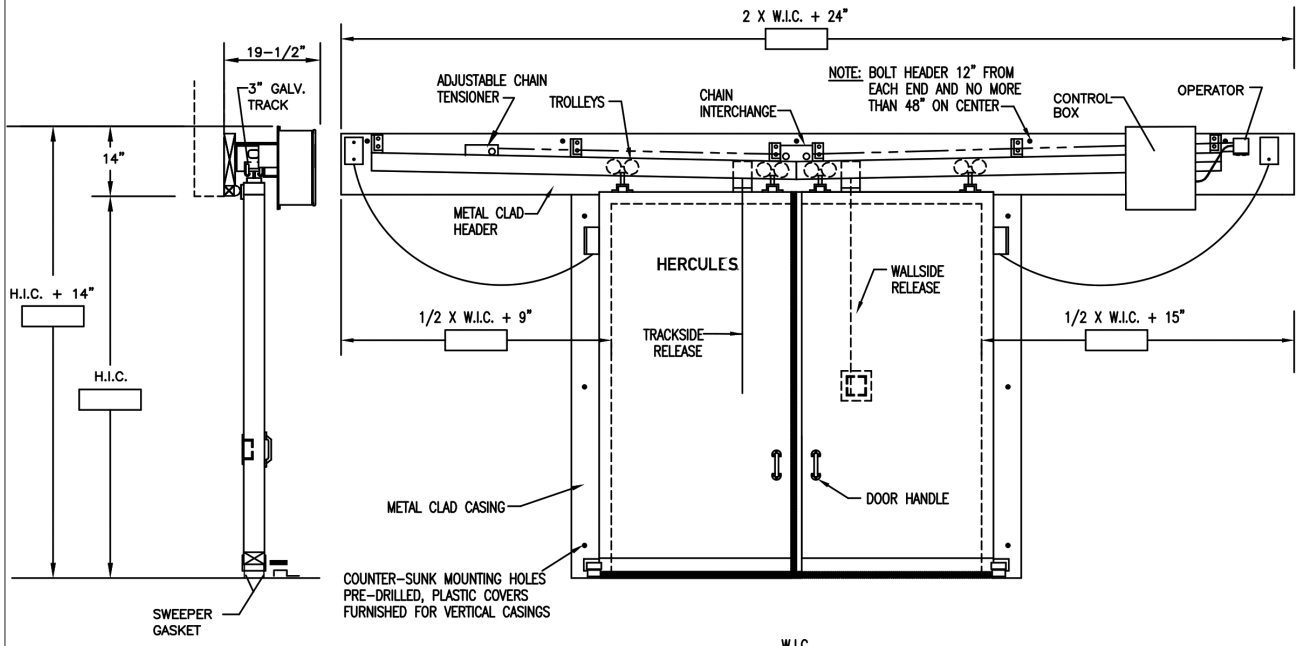

NOTE: ALL FREEZER DOORS MUST HAVE SEPERATE 120 VOLT SUPPLY FOR HEATER CABLES FOR EACH DOOR

INSTALLATION REQUIREMENTS

I. THE FLOOR UNDER THE DOOR MUST BE LEVEL AND SMOOTH

II. THE WALL BEHIND THE DOOR FRAME MUST BE SMOOTH AND IN A COMMON PLANE

DOOR PANEL AND FRAME

1. DOOR THICKNESS
   - ☐ 4"
   - ☐ 6" (FREEZER ONLY)
2. TEMPERATURES
   - WALL SIDE _____ °F
   - HINGESIDE _____ F
3. SLIDE DIRECTION
   - ☐ LEFT
   - ☐ RIGHT
4. PANEL AND FRAME CLADDING
   - ☐ WHITE STUCCO EMBOSSED GALV STEEL
   - ☐ MILL FINISH STUCCO EMBOSSED STEEL
   - ☐ STAINLESS STEEL
   - ☐ SANDSTONE STUCCO EMBOSSED GALV STEEL
   - ☐ WHITE STUCCO EMBOSSED ALUMINUM
   - ☐ MILL FINISH STUCCO EMBOSSED ALUMINUM
5. JAMBS
   - JAMB DEPTH _____
   - ☐ HDPE CLAD IN SAME MATL AS DOOR
   - ☐ CHANNEL TRIM
   - ☐ OTHER
6. OPERATOR
   - ☐ STANDARD OPERATOR
   - ☐ HIGH SPEED OPERATOR

OPTIONS

7. ☐ FREEZER DOOR
   HEATER WIRE RUN AROUND PERIMETER OF DOOR LEAF ON WALLSIDE
8. ☐ INSIDE CASINGS
9. ☐ HOOD
   - ☐ MATCHED TO FACE OF DOOR
   - ☐ OTHER
10. ☐ KICKPLATES
    - ☐ HINGESIDE
    - HEIGHT: ☐ 18" ☐ 24" ☐ 36" ☐ 48" ☐ OTHER
      - ☐ ALUMINUM DIAMOND PLATE
      - ☐ 18 GA. STAINLESS STEEL
      - ☐ 16 GA. GALV. STEEL
      - ☐ OTHER
11. ☐ VISION PANEL
    - ☐ 12" X 12" INSULATED
    - ☐ 12" x 12" HEATED
    - ☐ OTHER
12. ☐ LOCKING DEVICE
    - ☐ TRACKSIDE ☐ WALLSIDE
      - ☐ WITH POWER CUTOFF AND SAFETY RELEASE
      - ☐ WITH POWER CUTOFF – NO SAFETY RELEASE
13. ☐ RADIO CONTROL
14. ☐ PHOTOCELL
    ☐ TO OPEN ☐ AS SAFETY
15. ☐ MOTION DETECTOR
    ☐ TO OPEN ☐ AS SAFETY
16. ☐ LOOP DETECTOR
    ☐ TO OPEN ☐ AS SAFETY
17. ☐ TIMER DELAY CLOSE

	DOOR NO.	QTY.	W.I.C.	H.I.C.	USE	VOLTAGE	LOCK	SAFETY RELEASE	FINISH COVERING	FINISH GAGE	

HERCULES
A SENNECA COMPANY

ELECTRIC BI-PARTING SLIDING DOOR

SCALE: NONE		DRAWN BY
DATE:		
For:		Job No.
		DRAWING NUMBER
